PROJECT PLANNING/SCHEDULE

Client Name : Executive Engineer BBMP RR Nagara Division, Bangalore

Project Name : Comprehensive Development of Roads & Drains in JP Park, Yeshawanthapura, Jalahalli and Surrounding areas in W No.16, 17 and 37 under PACKAGE- 2022-23 RRN-DEV-(15)

Project Start Date : 29-Sep-22

Project End Date : 28-Mar-23

Project Length in Days : 180

Sl. No	Assignment	Unit	Boq Qnty	Start Date	End Date	No. of Working Days
1	Removing & Refixing stone slabs of drains and pointing in C.M (1:3) Data Rate	Sqm	23636.94	1-Oct-22	5-Nov-22	35
2	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, key trenches, foundation of bridges and such similar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution belts	Cum	17634.54	8-Oct-22	12-Nov-22	35
3	Providing and laying in position plain cement concrete Mix 1:5:6 (M10) Using 40 mm nominal size graded crushed coarse aggregates for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS	cum	162.70	20-Oct-22	24-Nov-22	35
4	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x200x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572:2005 including cost of all materials, labour, scaffolding and curing, usage charges of machinery etc complete as per specifications.I.No 6.32 P.No 17 Volume- 2 SR 2021-22	Sqm	13610.70	18-Oct-22	27-Nov-22	40
5	Providing Flush/ Ruled pointing: Pointing on stone work with cement mortar 1:3 (1 cement : 3 fine sand) after raking joints to depth nicely lining, including cost of materials, labour, curing as per specifications and as per directions of Engineer-in-charge.Item No.8.19.1,Page No.44, Vol II SR 21-22	Sqm	10787.18	18-Oct-22	27-Nov-22	40
6	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150 mm thickness, well compacted using plate vibrators, including all lead & lifts, cost of all materials of quality, labour Usage charges of	Cum	945.78	30-Oct-22	14-Dec-22	45
7	Providing B S Slabs of selected quality roughly dressed having a size of 10cms thick and fixed in cement mortar (1:6) including fixing curing etc., complete.as directed by the Engineer in Charge of the work (Excluding GST and Area Leading Charges)	Sqm	13892.46	13-Oct-22	17-Nov-22	35
8	Providing one line dressing to granite stone slab / granite stone masonry as per specifications. as directed by the Engineer in Charge of the work	Sqm	13892.46	28-Oct-22	2-Dec-22	35

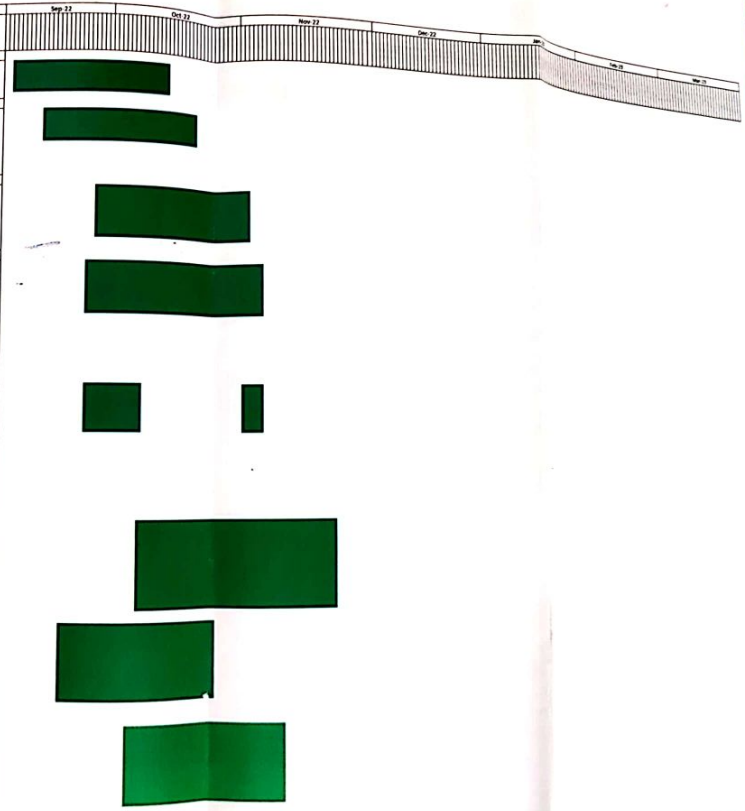

Scanned with CamScanner

Assignment		Req Qnty	Start Date	End Date	No. of Working Days
...ing (Civil Area Leading Charges)					
...ing (Chowkidar)	Sqm	14711.00			
...ing (Chowkidar)	Sqm	2169.36	12-Nov-22	22-Dec-22	40
...ing (Chowkidar)	Nos	1799.00	27-Nov-22	6-Jan-23	40
...ing (Chowkidar)	Nos	900.00	2-Dec-22	11-Jan-23	40
...ing (Chowkidar)			17-Dec-22	16-Jan-23	30

Scanned with CamScanner
